
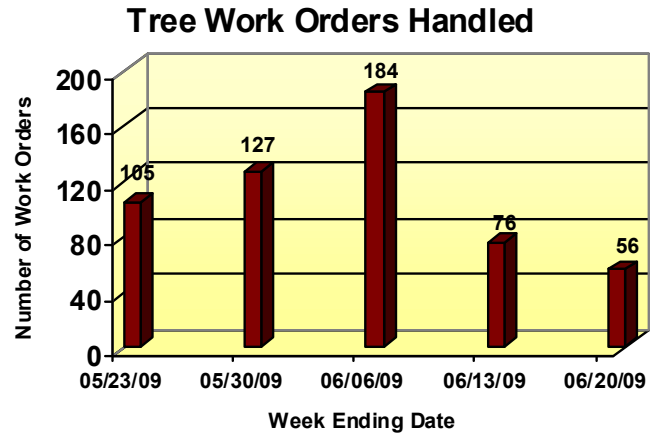


Department of Parks and Parkways

Weekly Progress Report

Week Ending June 20, 2009

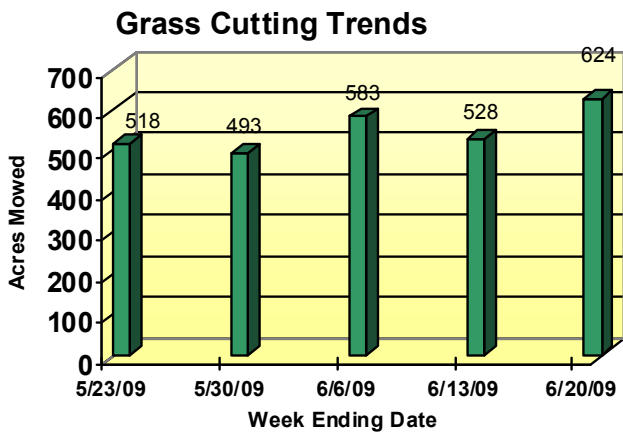

Please Note:

- There were shelter rentals in Joe Brown Park on June 20th.
- Lafayette Square Concert Series “Wednesdays at the Square” was held on June 17th.
- 200 man hours were lost due to sick or annual leave and leave without pay.
- Parkway’s crews (32 man hours) were used to remove signs from the neutral grounds citywide.
- The extreme heat and drought conditions citywide have Parkway’s water truck watering trees and plant material in an effort to keep them alive. Hats off to Parkway’s Grounds Maintenance and Forestry crews for their endurance and dedication during the extreme heat condition they’re experiencing in the field.
- We remain facility challenged. Because of the slow progress of the repair of Parkway’s Gentilly Facilities, Grounds Maintenance is still operating out of the small Algiers Substation. This continues to pose logistical, productivity and security problems. Greenhouse continues to struggle with no power and no watering system.
- Parkway’s reviewed and/or provided input for the following projects: 628 Orange St. tree planting, 1015 S. Carrollton Avenue tree planting, Lusher Elementary School planting plan, Palmer Park grant application plan, Entergy utility work permits, Pontchartrain Park master plan, Citywide Neutral Ground Planting Plan, 231 N. Rampart tree planting, Bayou Road pre-design phase and Brechtel Park Picnic Shelters.

Parks & Parkways (In-house Crews) Projected Schedule /Week Ending July 4th

Rampart Street	4.0	Richard Lee Playground	2.6
Esplanade Avenue and lot	7.7	Goins Playground	.1
Gayerre Park	.1	Oliver Bush Park	4.5
Capdeville Place	.4	Delery Park	2.0
Kruttchsnette Park	.1	Schabel Playground	.3
Washington Square Park	2.5	O’Dile Davis Playground	2.7
St. Roch Avenue	2.0	Pete Sanchez Health Clinic	.8
Behrman Park	57.7	Roffignac Playground	.4
Touro/Shakespeare Campus	3.9	Gertown Pool	1.0
Gen. DeGaulle Blvd.	66.0	M. L. King Blvd.	7.0
Hardin Park	2.4	6 th District Police Station	.1
Katherine Benson Health Clinic	.01	Keller Center	.7
Brake Tag Station @ Lafitte	1.3	Hollygrove Center	.2
Cadiz Park	.2	St. John Court	.01
City Park Avenue	2.0	Metairie Road	1.0
MTA @ City Park Avenue	1.0	Fire Communication Tower	1.7

Department of Parks and Parkways

Weekly Progress Report

Week Ending June 20, 2009

Page 2

Delgado/Kirsch Rooney Circle	5.4	Kirsch Rooney	1.3
Nashville Avenue	1.0	Broadway	2.0
Broad Place	.1	Jackson Avenue	.5
Sophie B. Wright	.2	N/S Broad Street	12.0
Keller Library	.9	Police Headquarter	1.0
D. A. Parking Lot	1.1	Gravier Park	.3
Criminal Court Building	1.0	Broad Street Gas Station	1.0
Lyons Center (planters)	3.2	<u>Total Acreage Scheduled</u>	207.0

Ramelli - Contractor's Projected Schedule / Parks/ Week Ending July 4th

Brignac Playspot	1.0	Leo Benewell Playspot	1.0
Broadmoor Playspot	1.0	Soraparu Playspot	1.0
Danneel Playspot	1.0	Delcazel Playground	1.0
Dublin Park	1.0	Donsereaux/Harrison Playground	2.0
Larkin Playground	1.0	Fox Playground	3.0
Evans Playground	2.0	East Shore Playground	4.0
Digby Playground	6.0	St. Roch Park	5.0
Carver Playground	2.0	Treme Center	1.0
St. Bernard Recreation Center	1.0	Harrell Park & Pool	5.0
Lemann Pool	4.0	Lyons Center & Pool	1.0
Mickey Markey	1.0	St. Patrick Playground	2.0
Sam Bonart	2.0	Joe W. Brown Park (open side)	20.0
Behrman Stadium	3.0	Kenilworth Playground	4.0
Bodenger Playground	6.0	Milne Playground	3.0
Cut-Off Playground	6.0	Pontchartrain Playground	20.0
McDonough Playground	3.0	Village delis Playground	4.0
Norman Playground	6.0	Willie Hall Playground	2.0
Easton Playground	3.0	Annunciation Playground	4.0
Hunter's Field	2.0	Burke Playground	3.0
Sampson Playground	2.0	Conrad Playground	3.0
Stallings Playground - Gentilly	2.0	Norwood Thompson Playground	3.0
Barrow Stadium	3.0	Taylor Playground	4.0
Ideal Place Playspot	1.0	Marie Gorette Playground	2.0
Kerry Curley Playground	2.0	Pradot Playground	3.0
Kingswood Playspot	3.0	Robert Playground	3.0
Peace Playground	1.0	Wembledon Playground	4.0
Boe Playspot	1.0	Cabrini Playspot	1.0
Donnelly Playground	2.0	F. P. Jackson Playspot	1.0
Gatto Playspot	1.0	Mirabeau Playspot	1.0

Department of Parks and Parkways

Weekly Progress Report

Week Ending June 20, 2009

Page 3

Oak Park Playground	3.0	Rome Playspot	1.0
St. James Playspot	1.0	Union Playspot	2.0
		<u>Total Acreage Scheduled</u>	188.0

Ramelli - Contractor's Projected Schedule / Neutral Grounds / Week Ending July 4th

Canal Street	9.0	LaSalle/Simon Bolivar	6.0
Earhart Blvd.	14.0	Louisiana Avenue	3.0
Fontainebleau Drive	2.0	Napoleon Avenue	16.0
Jefferson Avenue	3.0	S. Claiborne Avenue	27.0
Jefferson Davis Parkway	18.0	Washington/Toledano Street	11.0
		<u>Total Acreage Scheduled</u>	109.0
